


Route 121 / 460 ADHS Corridor Q

PROJECT STATUS

Not to Scale
Subject to Ongoing Reviews and Approvals

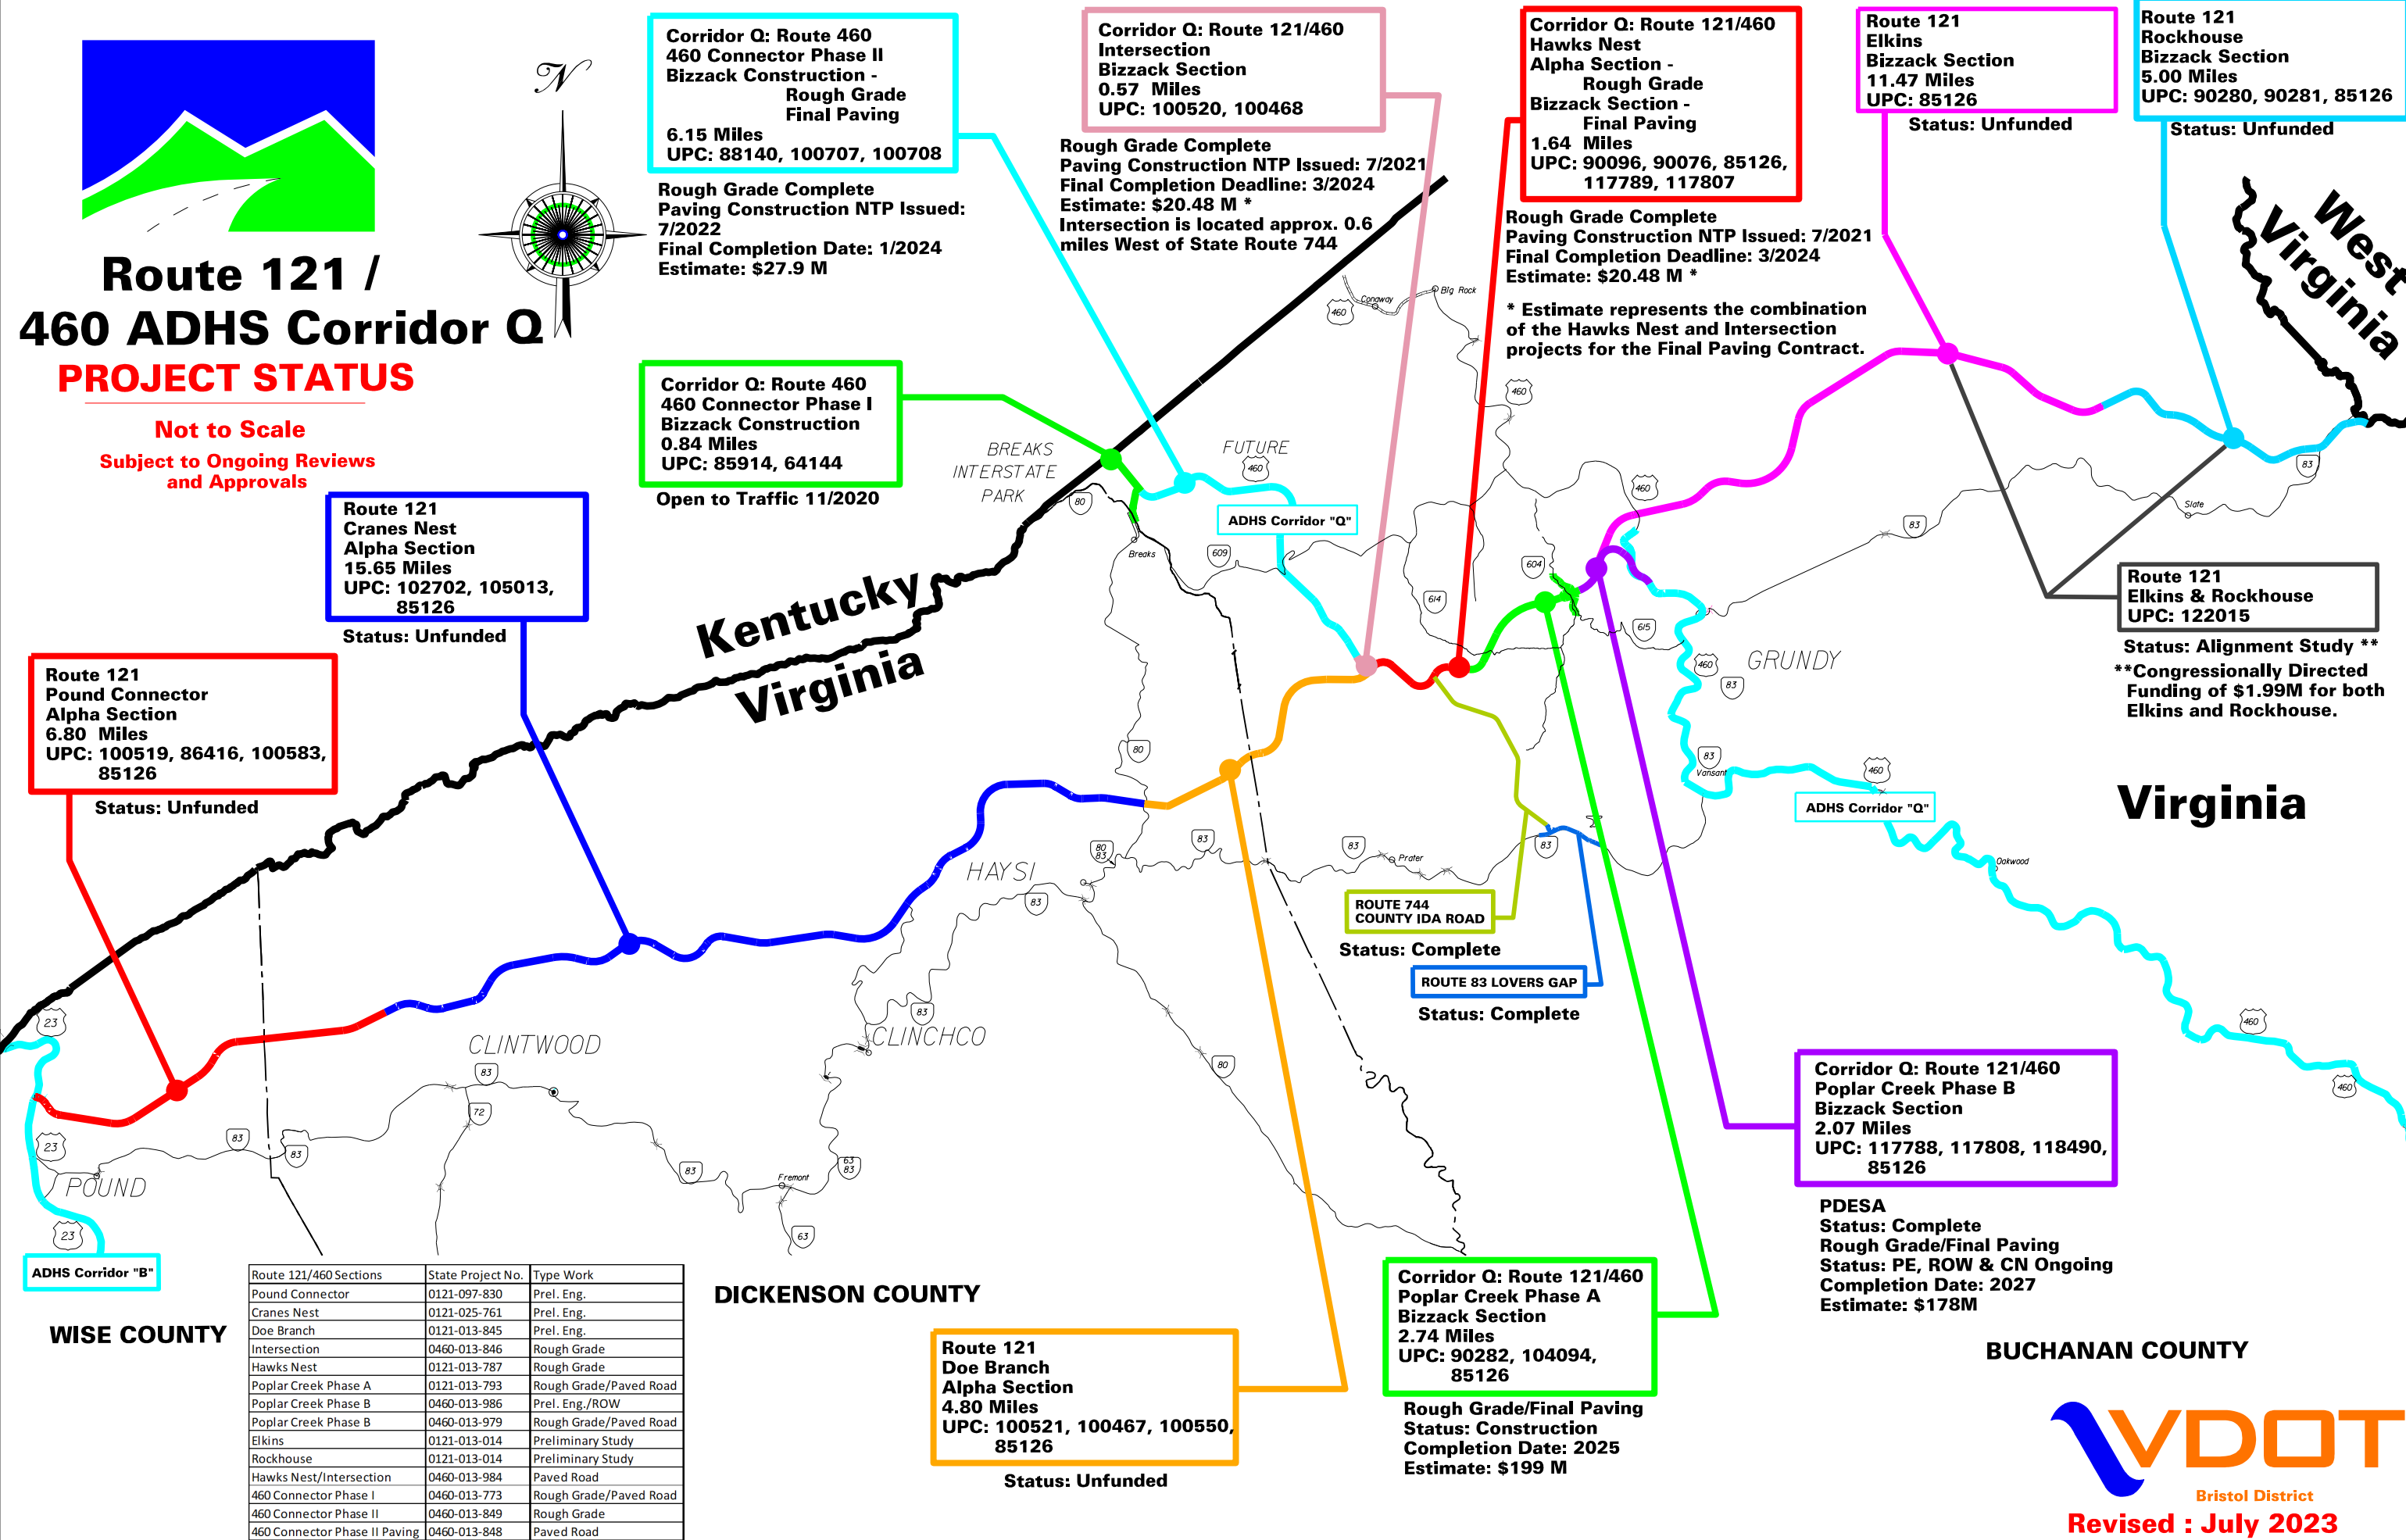

Corridor Q: Route 460 460 Connector Phase II Bizzack Construction - Rough Grade Final Paving
 6.15 Miles
 UPC: 88140, 100707, 100708
 Rough Grade Complete
 Paving Construction NTP Issued: 7/2022
 Final Completion Date: 1/2024
 Estimate: \$27.9 M

Corridor Q: Route 121/460 Intersection Bizzack Section
 0.57 Miles
 UPC: 100520, 100468
 Rough Grade Complete
 Paving Construction NTP Issued: 7/2021
 Final Completion Deadline: 3/2024
 Estimate: \$20.48 M *
 Intersection is located approx. 0.6 miles West of State Route 744

Corridor Q: Route 121/460 Hawks Nest Alpha Section - Rough Grade Bizzack Section - Final Paving
 1.64 Miles
 UPC: 90096, 90076, 85126, 117789, 117807
 Rough Grade Complete
 Paving Construction NTP Issued: 7/2021
 Final Completion Deadline: 3/2024
 Estimate: \$20.48 M *

Route 121 Elkins Bizzack Section
 11.47 Miles
 UPC: 85126
 Status: Unfunded

Route 121 Rockhouse Bizzack Section
 5.00 Miles
 UPC: 90280, 90281, 85126
 Status: Unfunded

Corridor Q: Route 460 460 Connector Phase I Bizzack Construction
 0.84 Miles
 UPC: 85914, 64144
 Open to Traffic 11/2020

Route 121 Cranes Nest Alpha Section
 15.65 Miles
 UPC: 102702, 105013, 85126
 Status: Unfunded

Route 121 Pound Connector Alpha Section
 6.80 Miles
 UPC: 100519, 86416, 100583, 85126
 Status: Unfunded

Route 121 Elkins & Rockhouse
 UPC: 122015
 Status: Alignment Study **
 **Congressionally Directed Funding of \$1.99M for both Elkins and Rockhouse.

ROUTE 744 COUNTY IDA ROAD
 Status: Complete

ROUTE 83 LOVERS GAP
 Status: Complete

Corridor Q: Route 121/460 Poplar Creek Phase B Bizzack Section
 2.07 Miles
 UPC: 117788, 117808, 118490, 85126
 PDESA
 Status: Complete
 Rough Grade/Final Paving
 Status: PE, ROW & CN Ongoing
 Completion Date: 2027
 Estimate: \$178M

Corridor Q: Route 121/460 Poplar Creek Phase A Bizzack Section
 2.74 Miles
 UPC: 90282, 104094, 85126
 Rough Grade/Final Paving
 Status: Construction
 Completion Date: 2025
 Estimate: \$199 M

Route 121 Doe Branch Alpha Section
 4.80 Miles
 UPC: 100521, 100467, 100550, 85126
 Status: Unfunded

Route 121/460 Sections	State Project No.	Type Work
Pound Connector	0121-097-830	Prel. Eng.
Cranes Nest	0121-025-761	Prel. Eng.
Doe Branch	0121-013-845	Prel. Eng.
Intersection	0460-013-846	Rough Grade
Hawks Nest	0121-013-787	Rough Grade
Poplar Creek Phase A	0121-013-793	Rough Grade/Paved Road
Poplar Creek Phase B	0460-013-986	Prel. Eng./ROW
Poplar Creek Phase B	0460-013-979	Rough Grade/Paved Road
Elkins	0121-013-014	Preliminary Study
Rockhouse	0121-013-014	Preliminary Study
Hawks Nest/Intersection	0460-013-984	Paved Road
460 Connector Phase I	0460-013-773	Rough Grade/Paved Road
460 Connector Phase II	0460-013-849	Rough Grade
460 Connector Phase II Paving	0460-013-848	Paved Road
